

Road Report July 2024

- Completed Work in June 2024
- Work in Process/Scheduled
- Thank you
- Decisions and Comments



Completed Work

- Road grading operations on various Township roads as noted
- All ROW mowing was completed prior to the end of June.
- The lack of maintenance in the ROW has been part of the issue with Lake 12 backing up. Emergency ditch cleaning helped alleviate the issue. Approximately 2800' was cleaned out and hauled away from Pioneer Road East of Partridge Road S. Another 1200' of ditch cleaning was done near White Birch Lane
- 7 compromised culverts were replaced on Pioneer Road
- Balsam Road box culvert was cleaned out from beaver activity plugging the water way
- Major construction on the Sturgeon Island Bridge cover has been completed. Remaining items left included electrical hook up and staining.



Grading 2024	Road Name	June		
CaCl2				
1E	Hill Street Road			
2E	Elm Tree Road			
3E	Northridge Road			
4E	Pioneer Road	6/13 & 6&14 East End		
5E	Partridge Road North			
6E	Partridge Road South		13-Jun	
7E	Lake 12 Road		13-Jun	
8E	Balsam Road			
9E	Birchview Road			
10E	Telker Road			
11W	Sunset Lane			
12W	Settlers Court			
13W	Lords Drive			
14W	Settlers Pond Drive			
15W	Paulus Road			
16W	Pine Tree Lane			
17W	Lakeshore Drive			
18E	Camp Farm Lane			
19E	Moss Lane			

Grading 2024	Road Name	February	March	April	May
CaCl2					
1E	Hill Street Road	2/7 Partial 2/21&22		11-Apr	5/10, 5/15,5/28
2E	Elm Tree Road	21-Feb		11-Apr	29-May
3E	Northridge Road	21-Feb		12-Apr	29-May
4E	Pioneer Road	2/7 & 2/21		5-Apr	5/22, 5/29
5E	Partridge Road North	2/7 & 2/21		10-Apr	5/16, 5/22, 5/28
6E	Partridge Road South	2/7 & 2/21		10-Apr	28-May
7E	Lake 12 Road	21-Feb		10-Apr	5/10, 5/15, 5/20, 5/28
8E	Balsam Road	2/7 & 2/21		10-Apr	28-May
9E	Birchview Road	21-Feb		10-Apr	5/10, 5/15, 5/16, 5/20, 5/28
10E	Telker Road	21-Feb		10-Apr	28-May
11W	Sunset Lane		11-Mar	12-Apr	29-May
12W	Settlers Court		11-Mar	12-Apr	29-May
13W	Lords Drive		11-Mar	12-Apr	5/20, 5/29
14W	Settlers Pond Drive		11-Mar	12-Apr	29-May
15W	Paulus Road		11-Mar	12-Apr	29-May
16W	Pine Tree Lane		11-Mar	12-Apr	29-May
17W	Lakeshore Drive	21-Feb	11-Mar	12-Apr	5/20, 5/29
18E	Camp Farm Lane	22-Feb		25-Apr	29-May
19E	Moss Lane	21-Feb		25-Apr	5/22, 5/28
20E	Brandt Road	21-Feb		25-Apr	28-May
21E	Sunrise View Road	21-Feb		25-Apr	28-May

Work in Process/Scheduled

- Sturgeon Island bridge County project has slowly resumed and is anticipated to be done in the fall of 2024
- Sturgeon Island Road asphalt project started May 8, 2024 and will be completed once the Sturgeon Island bridge project is done
- Township road sign and post replacement is scheduled for the Spring of 2025. They delay is because there is a backorder on posts and weather issues for the contractor.
- Culvert replacement on various Township Roads
- Ditch cleaning on various Township Roads



Thank you to our professional contactors.


Their hard work and cooperation is greatly appreciated!

- Kiminski Paving Inc.
- Dresel's Aggregate Inc.
- Jerry's Roadside Mowing
- Gobel Excavating & Aggregate Inc.
- Complete Carpentry, Robert Kenowski



Decisions and Comments

- Island Lake easement outlet discussion
- Brandt Road box culvert
- All road information and reports are located on The Windemere Township website

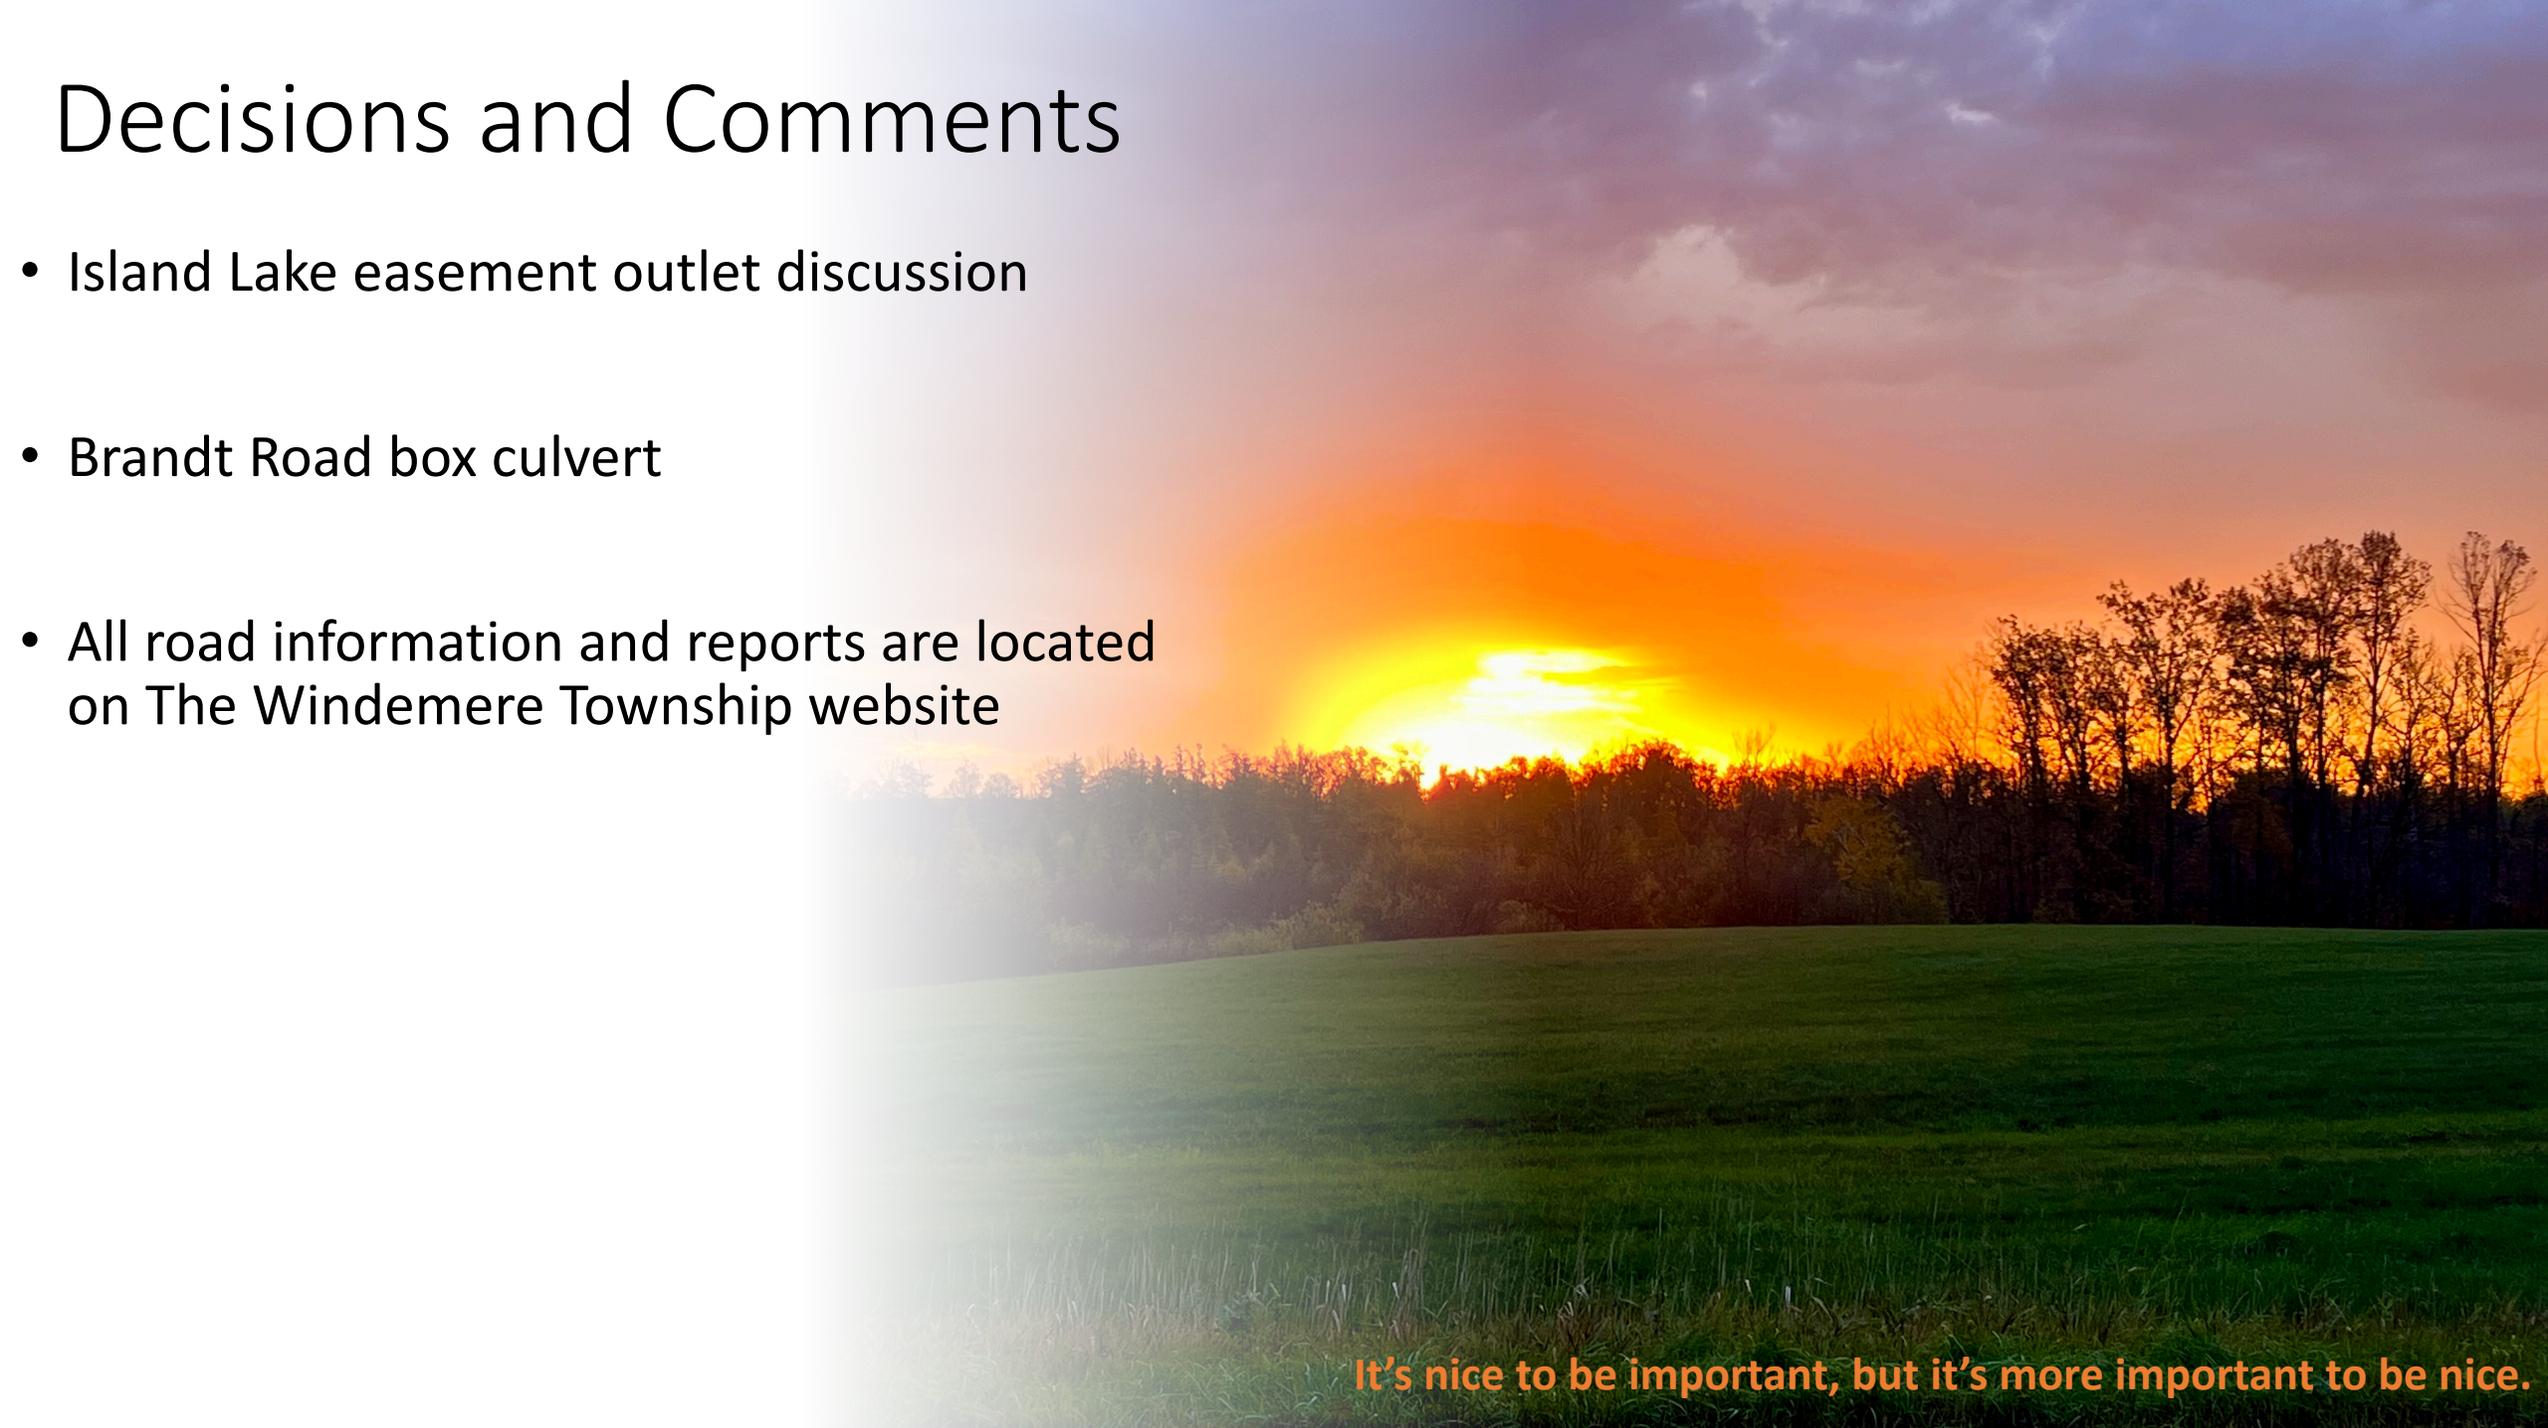

It's nice to be important, but it's more important to be nice.
